



# Druck-Setzungs-Versuch

## U5 Ost E

Bearbeiter: Ti

Datum: 10.02.17


Auftragsnummer: 021785

Entnahmestelle: B 59

Tiefe: 13,35

Labornummer: 24

Geolog. Bez.: Beckenschluff

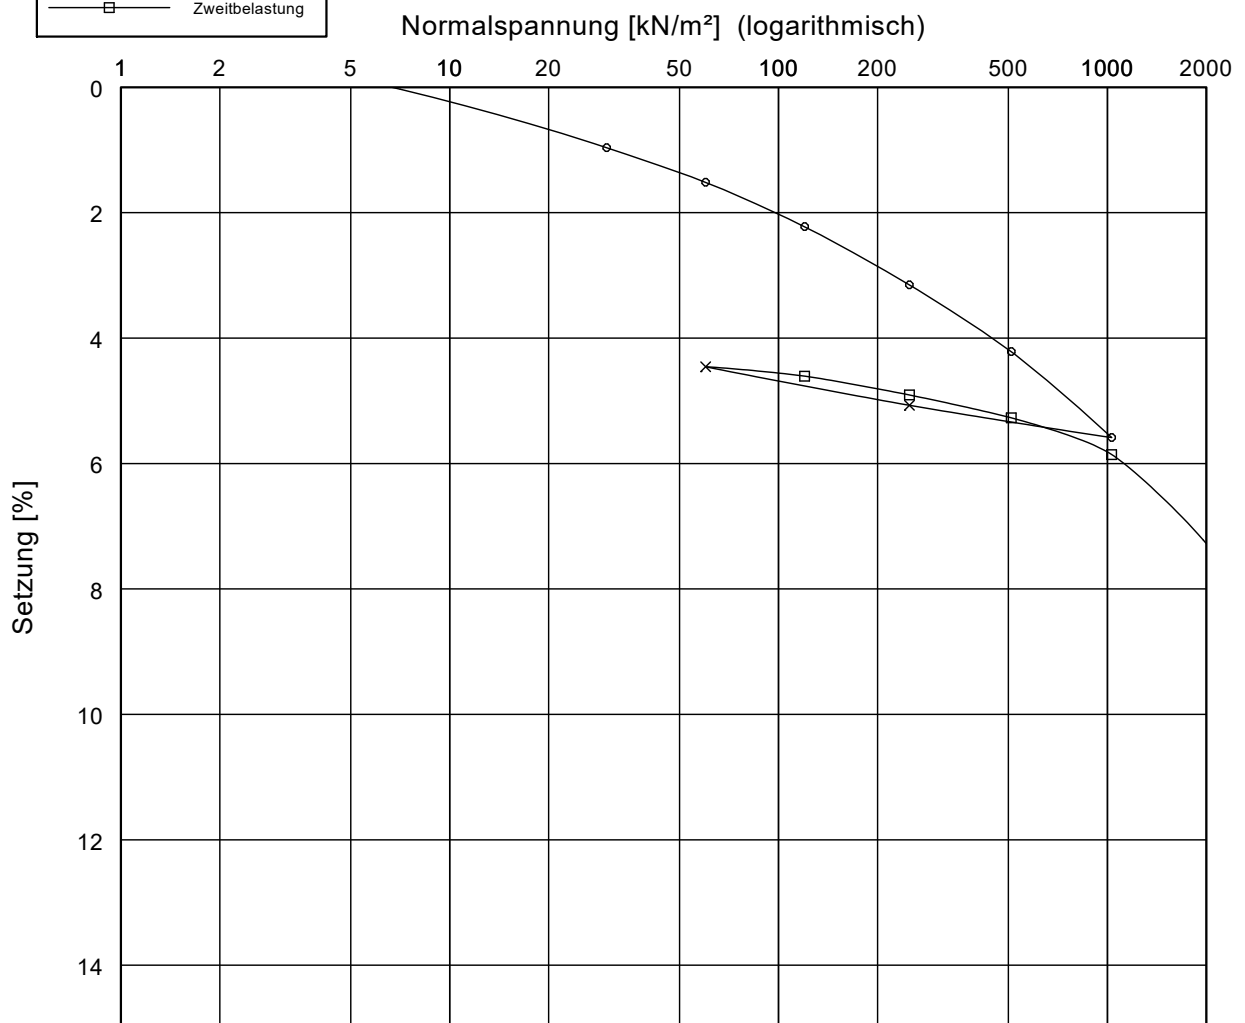

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Normalspannung [kN/m <sup>2</sup> ]	0.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.000	0.135	0.212	0.311	0.441	0.590	0.782	0.710	0.624	0.645	0.687	0.738	0.820	1.025
Steifemodul [MN/m <sup>2</sup> ]		3.1	5.5	8.5	14.0	24.4	37.9	-	-	40.0	43.3	71.4	88.8	68.3

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 26,3
Probendurchmesser [mm] = 70	w (nachher) [%] = 24,2
