



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 29.10.18

Auftragsnummer: 022445

Entnahmestelle: B 70-4/17


Tiefe [m]: 8,25

Labornummer: 25

Geolog. Bez.: Torf



Normalspannung [kN/m²] (logarithmisch)

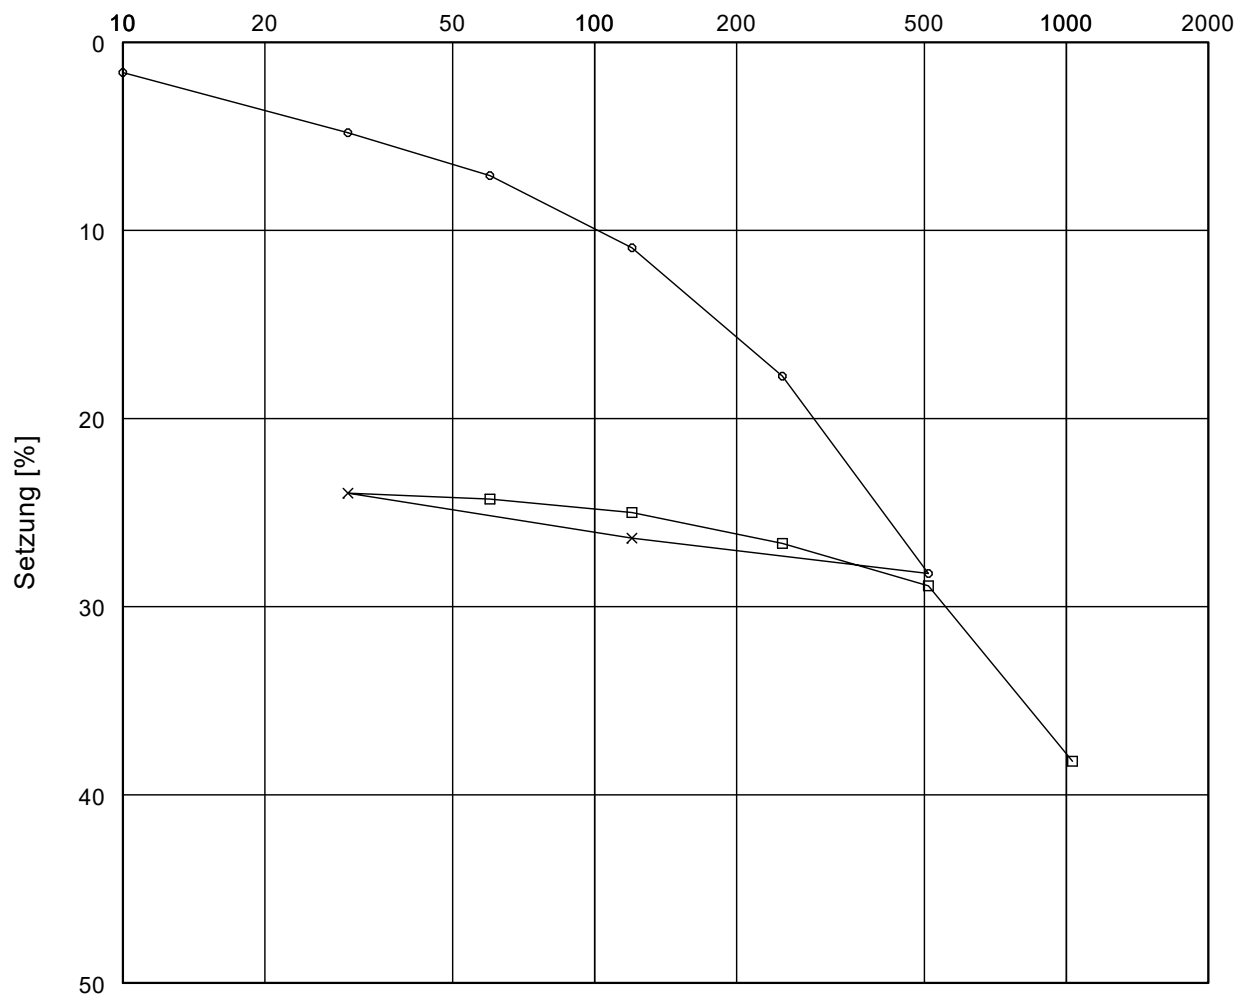

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13
Normalspannung [kN/m ²]	10.0	30.0	60.0	120.0	250.0	510.0	120.0	30.0	60.0	120.0	250.0	510.0	1030.0
Meßuhrablesung [mm]	0.226	0.673	0.992	1.530	2.485	3.953	3.690	3.356	3.400	3.500	3.729	4.045	5.350
Steifemodul [MN/m ²]		0.63	1.3	1.6	1.9	2.5	-	-	9.5	8.4	7.9	11.5	5.6

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 113,0
Probendurchmesser [mm] = 70	w (nachher) [%] = 103,3
