



# Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 08.01.18


Auftragsnummer: 021785\_4

Entnahmestelle: B 70

Tiefe: 21,35

Labornummer: 29

Geolog. Bez.: Beckenschluff

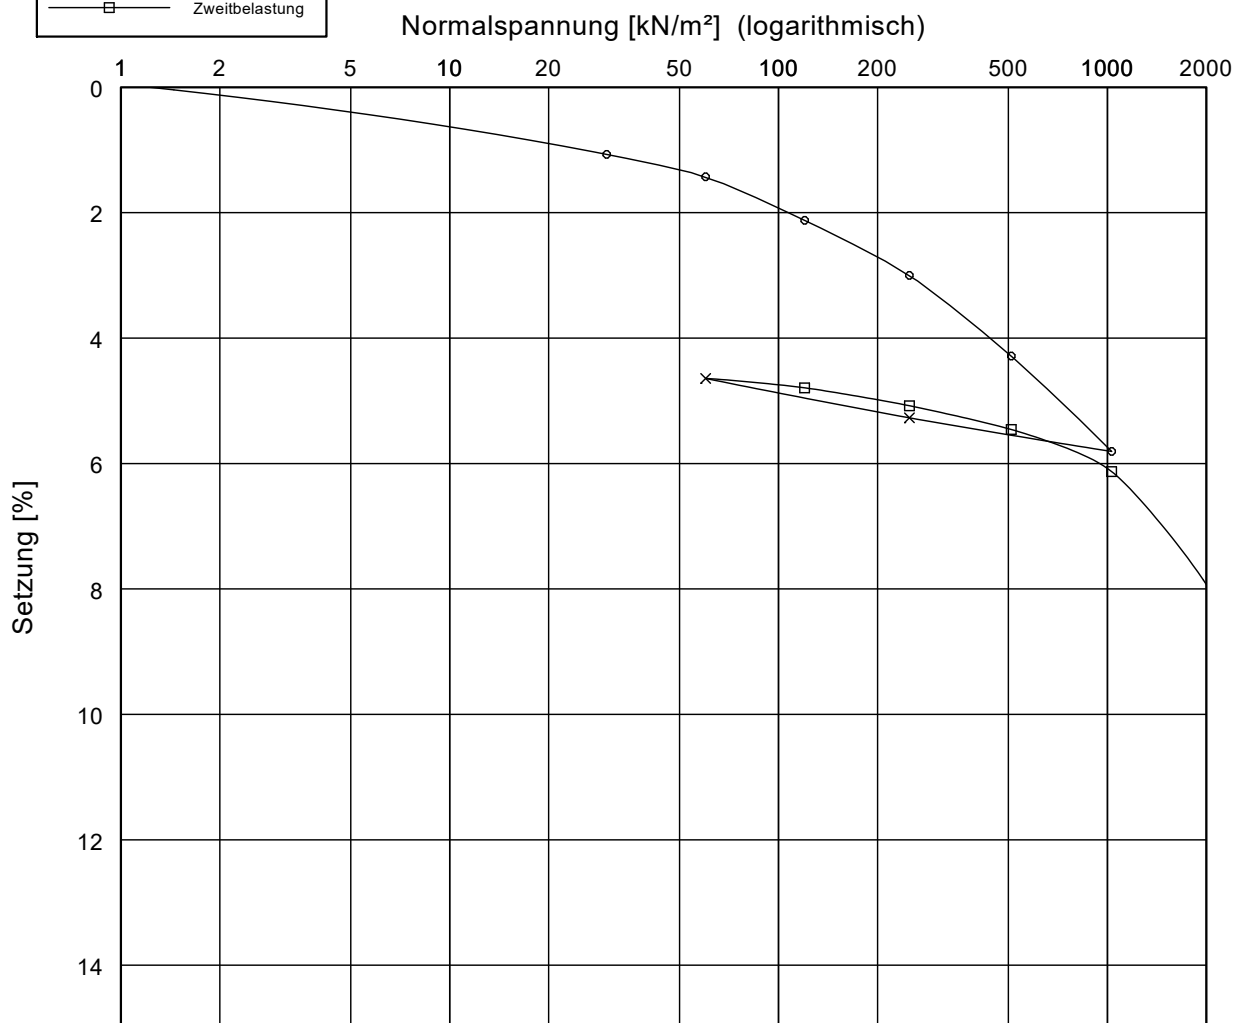

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Normalspannung [kN/m <sup>2</sup> ]	0.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.000	0.150	0.200	0.297	0.420	0.600	0.813	0.738	0.650	0.671	0.711	0.764	0.858	1.118
Steifemodul [MN/m <sup>2</sup> ]		2.8	8.4	8.7	14.8	20.2	34.2	-	-	40.0	45.5	68.7	77.4	53.8

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 26,9
Probendurchmesser [mm] = 70	w (nachher) [%] = 25,0
