



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 09.08.18


Auftragsnummer: 022445

Entnahmestelle: B 57/17


Tiefe: 15,25

Labornummer: 13

Geolog. Bez.: Beckenschluff, fS Str.



Normalspannung [kN/m²] (logarithmisch)

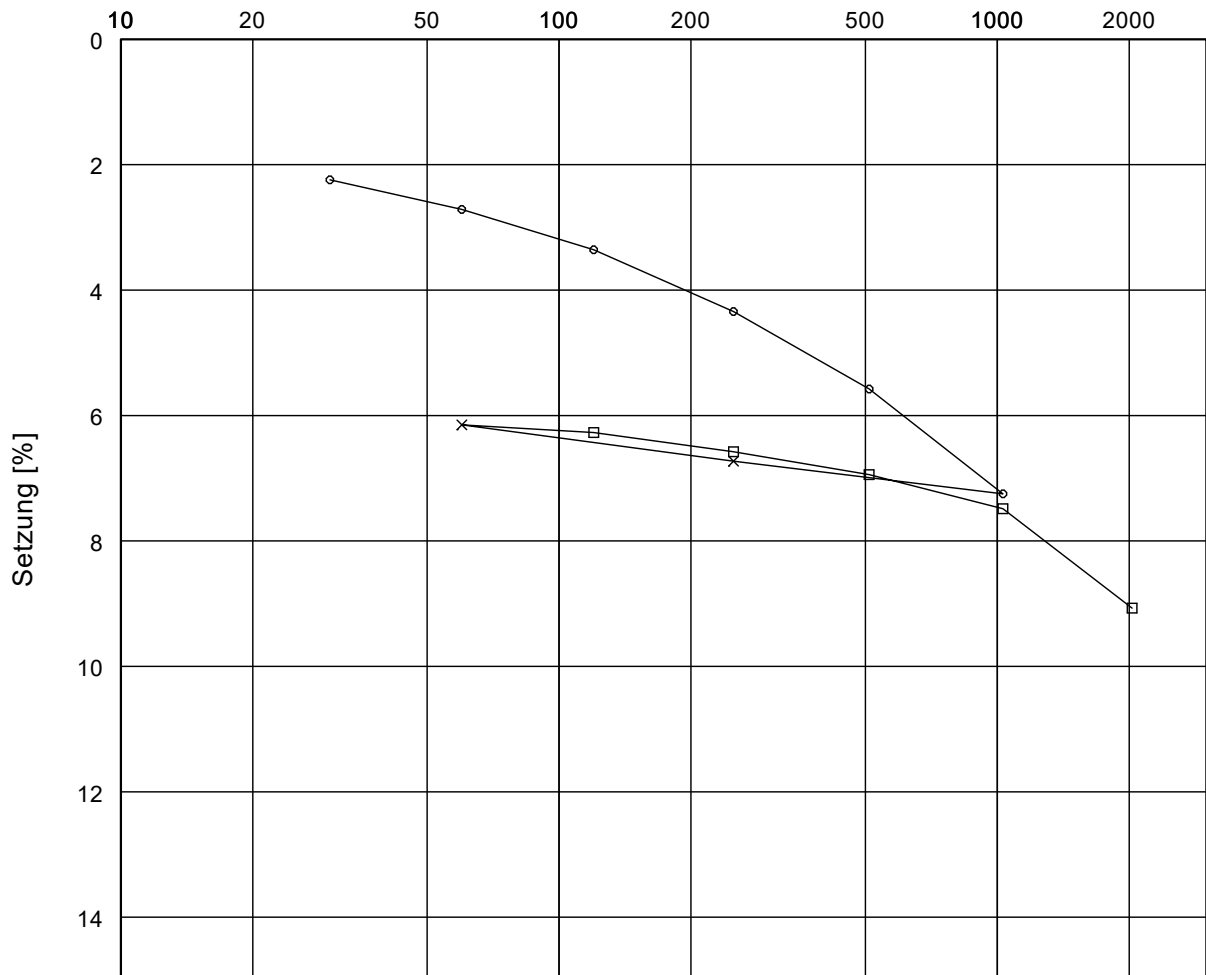

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13
Normalspannung [kN/m ²]	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.314	0.380	0.470	0.608	0.781	1.015	0.942	0.861	0.878	0.921	0.972	1.048	1.270
Steifemodul [MN/m ²]		6.4	9.3	13.2	21.0	31.1	-	-	49.4	42.3	71.4	95.8	63.1

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 27,3
Probendurchmesser [mm] = 70	w (nachher) [%] = 24,1
