



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 20.04.18


Auftragsnummer: 022445

Entnahmestelle: B 62/17


Tiefe: 13,75

Labornummer: 3

Geolog. Bez.: Beckenton, sandig



Normalspannung [kN/m²] (logarithmisch)

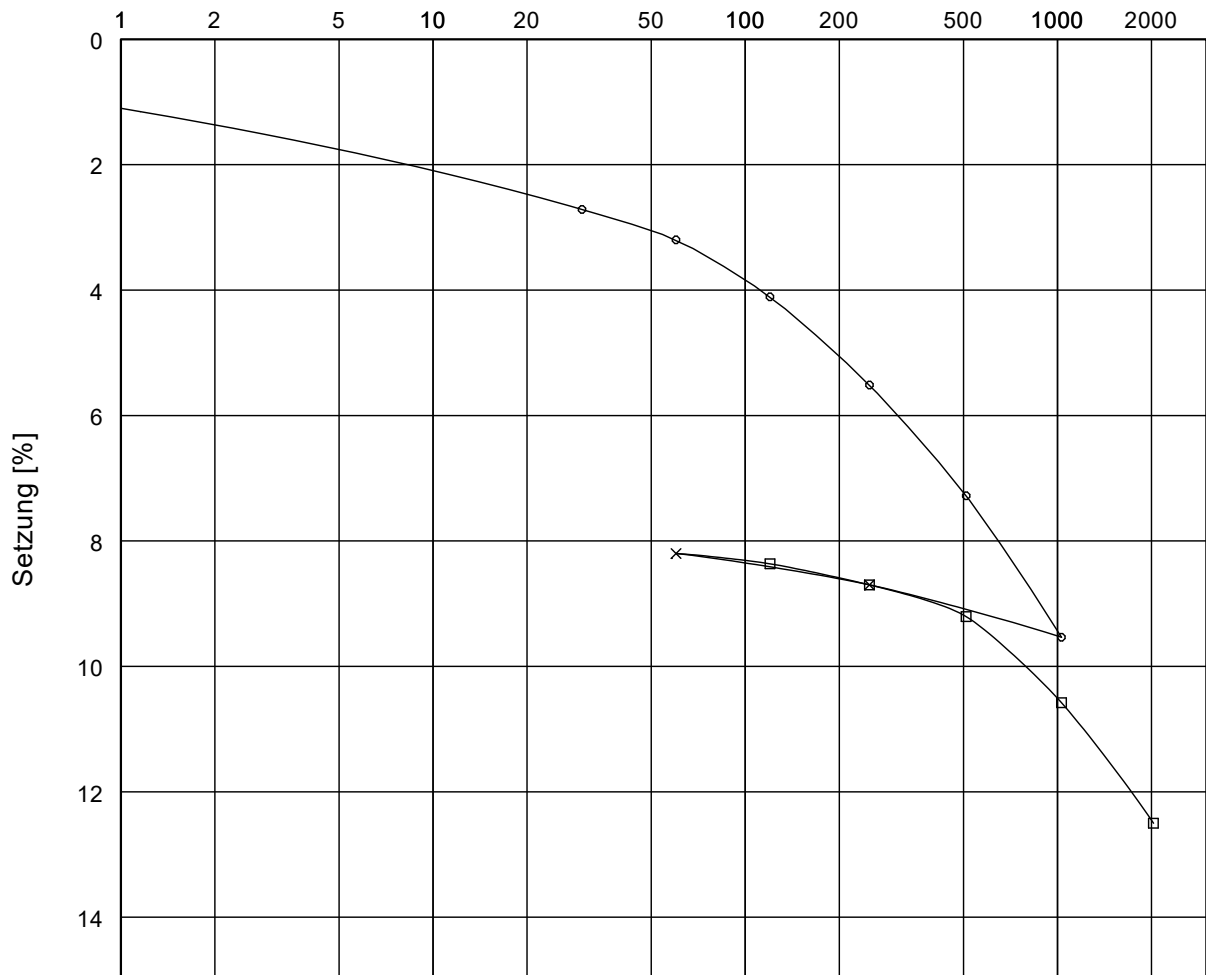

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Normalspannung [kN/m ²]	0.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.000	0.380	0.448	0.575	0.772	1.019	1.335	1.218	1.148	1.171	1.218	1.289	1.481	1.750
Steifemodul [MN/m ²]		1.1	6.2	6.6	9.2	14.7	23.0	-	-	36.5	38.7	51.3	37.9	52.0

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 25,4
Probendurchmesser [mm] = 70	w (nachher) [%] = 17,3
