



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 10.08.18

Auftragsnummer: 022445

Entnahmestelle: B 57/17


Tiefe: 25,25

Labornummer: 14

Geolog. Bez.: Geschiebemergel



Normalspannung [kN/m²] (logarithmisch)

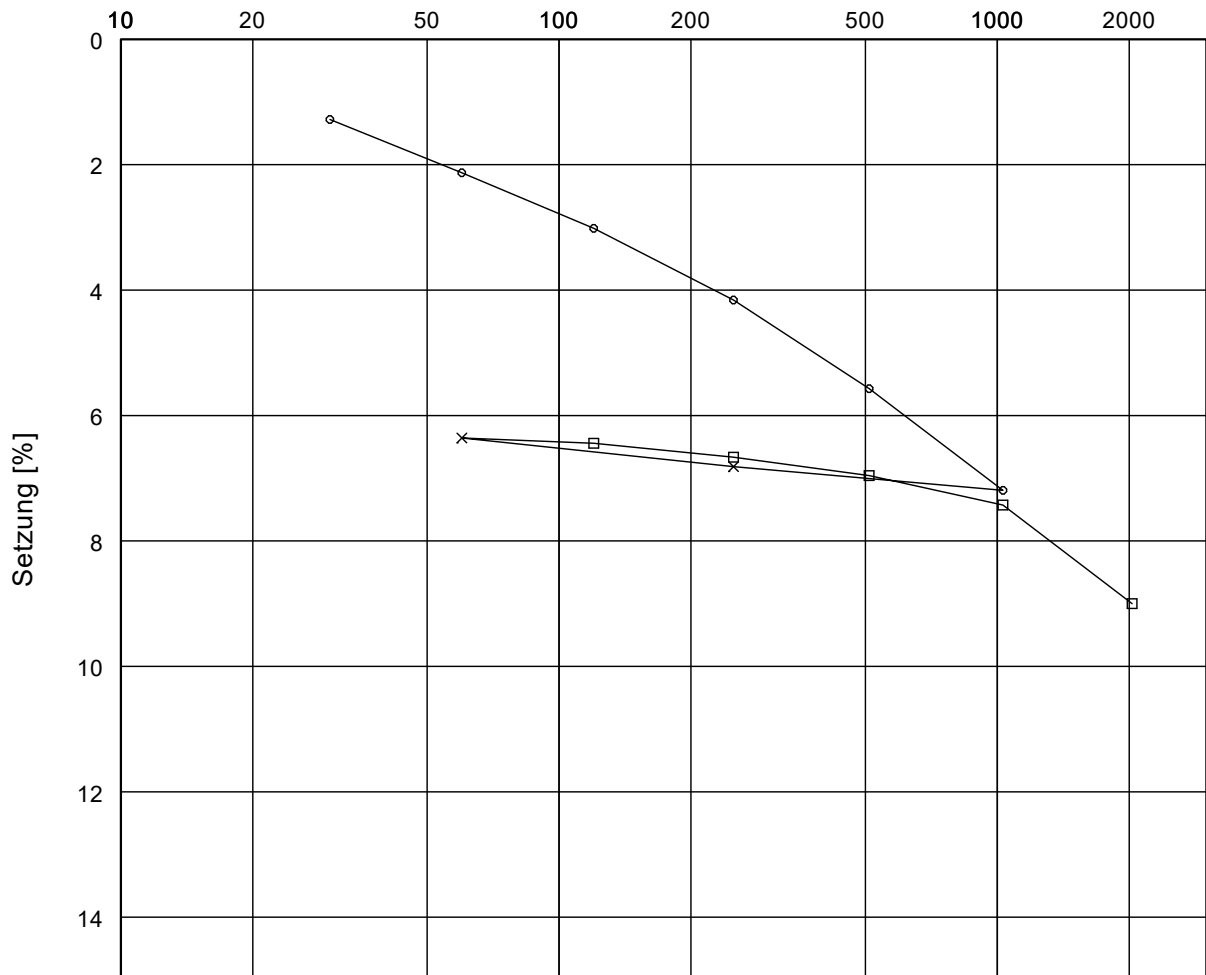

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13
Normalspannung [kN/m ²]	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.179	0.298	0.422	0.582	0.780	1.007	0.954	0.890	0.902	0.933	0.974	1.040	1.260
Steifemodul [MN/m ²]		3.5	6.8	11.4	18.4	32.1	-	-	70.0	58.7	88.8	110.3	63.6

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 10,6
Probendurchmesser [mm] = 70	w (nachher) [%] = 9,8
