



# Druck-Setzungs-Versuch

## U5 Ost E

Bearbeiter: Ti

Datum: 09.08.18


Auftragsnummer: 022445

Entnahmestelle: B 78-1/17


Tiefe: 34,75

Labornummer: 11

Geolog. Bez.: Lauenburger Ton



Normalspannung [kN/m<sup>2</sup>] (logarithmisch)

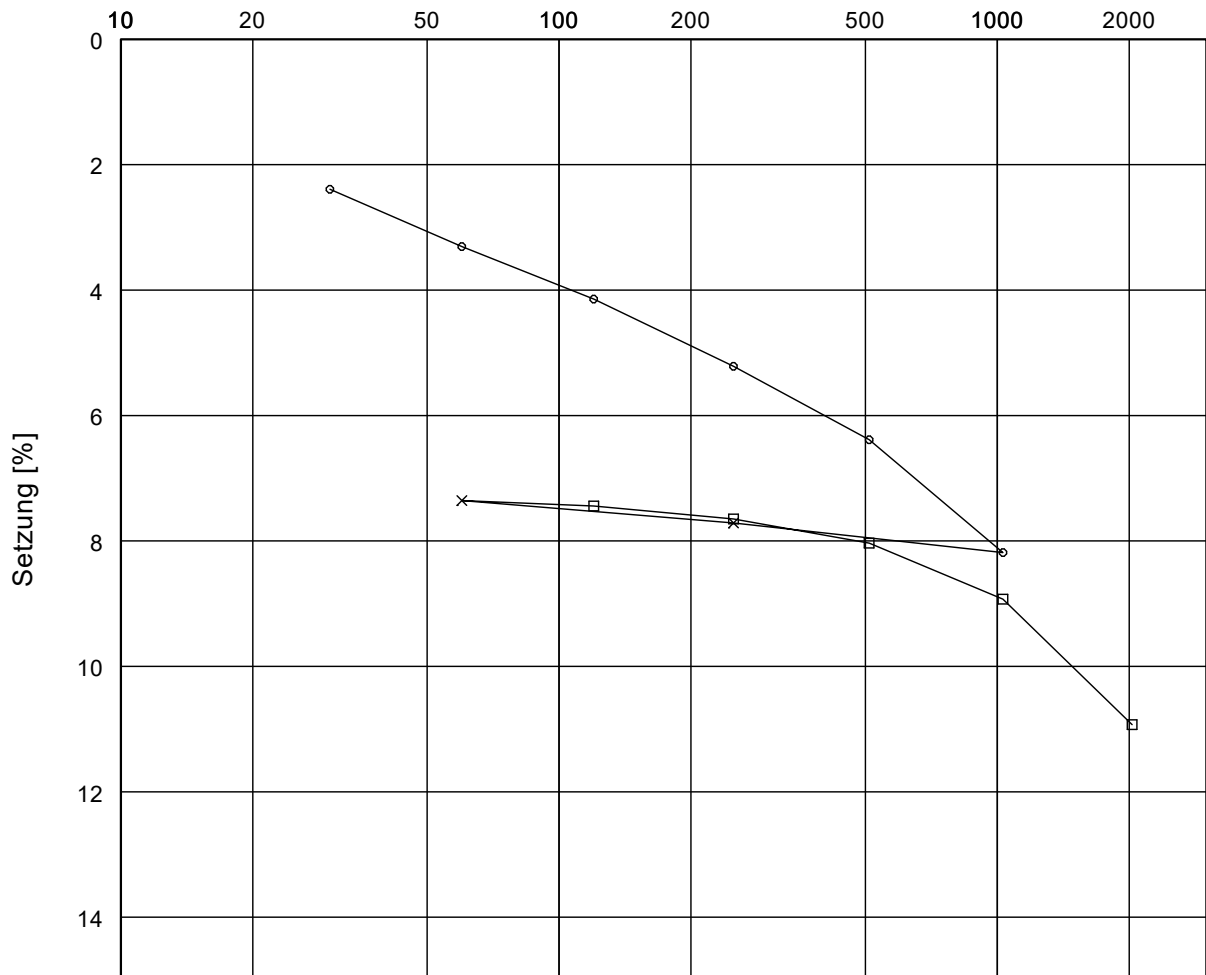

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13
Normalspannung [kN/m <sup>2</sup> ]	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.335	0.463	0.580	0.730	0.894	1.146	1.080	1.030	1.042	1.071	1.125	1.250	1.530
Steifemodul [MN/m <sup>2</sup> ]		3.3	7.2	12.1	22.2	28.9	-	-	70.0	62.8	67.4	58.2	50.0

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 23,6
Probendurchmesser [mm] = 70	w (nachher) [%] = 20,0
