



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Ti

Datum: 06.07.18


Auftragsnummer: 022445

Entnahmestelle: B 81/17


Tiefe: 14,25

Labornummer: 7

Geolog. Bez.: Geschiebemergel



Normalspannung [kN/m²] (logarithmisch)

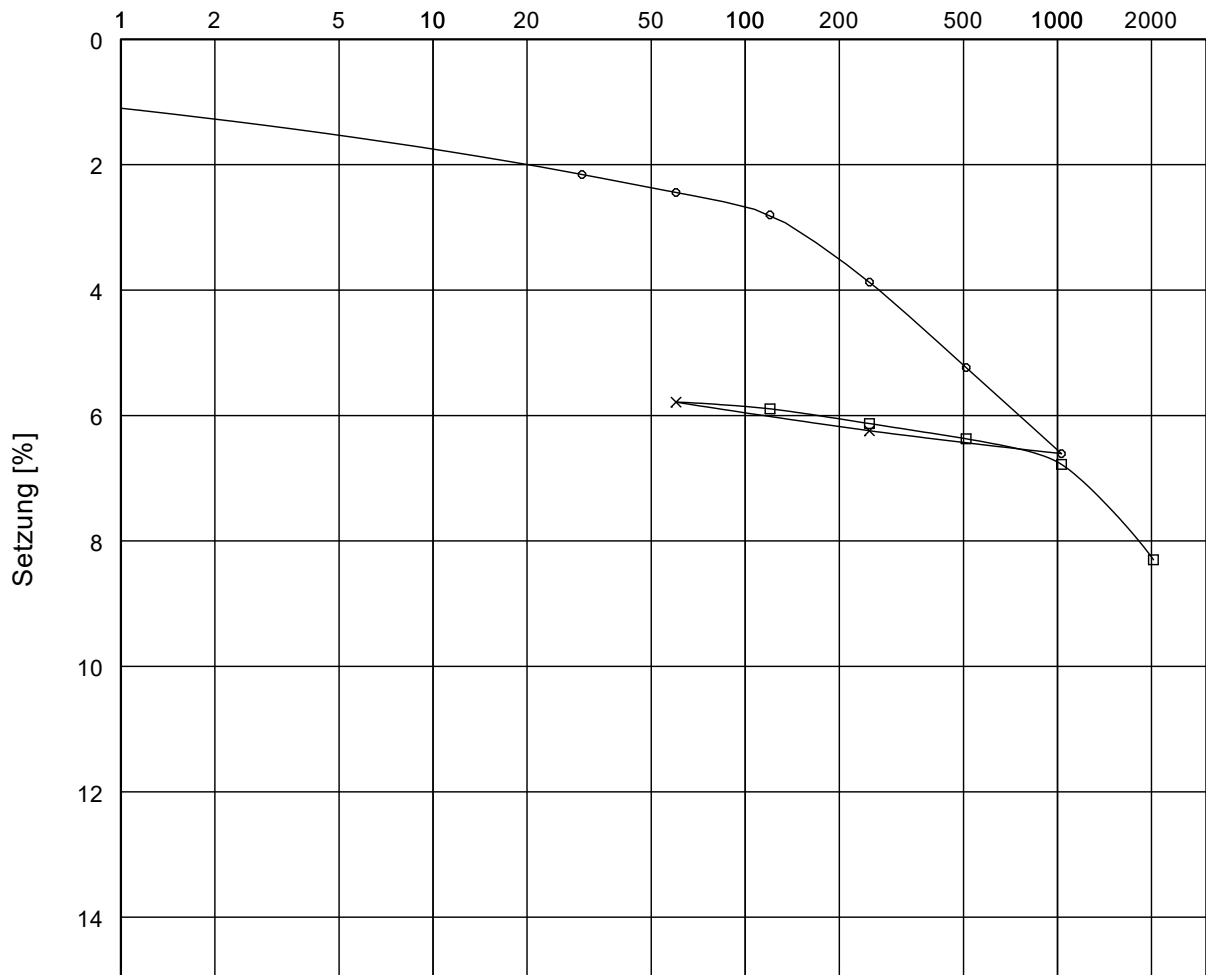

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Normalspannung [kN/m ²]	0.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.000	0.302	0.342	0.392	0.542	0.733	0.925	0.874	0.810	0.825	0.858	0.892	0.949	1.162
Steifemodul [MN/m ²]		1.4	10.5	16.8	12.1	19.1	37.9	-	-	56.0	55.2	107.1	127.7	65.7

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 11,8
Probendurchmesser [mm] = 70	w (nachher) [%] = 9,0
