



Druck-Setzungs-Versuch

U 5 Ost E

Bearbeiter: Boe

Datum: 21.09.18

Auftragsnummer: 022445

Entnahmestelle: B 86/17


Tiefe [m]: 15,45

Labornummer: 18

Geolog. Bez.: Geschiebemergel



Normalspannung [kN/m²] (logarithmisch)

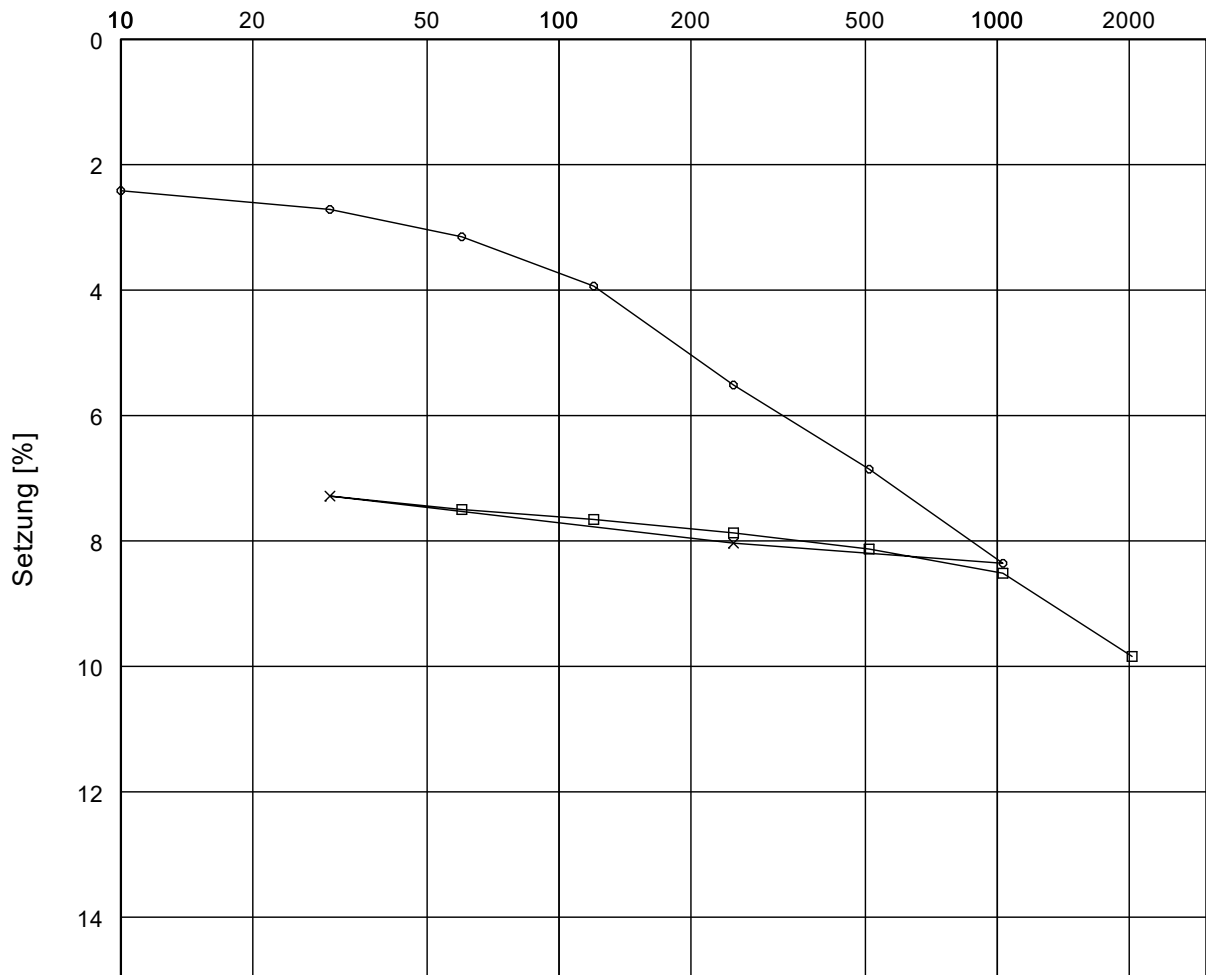

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
Normalspannung [kN/m ²]	10.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	30.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.338	0.380	0.441	0.551	0.772	0.960	1.170	1.125	1.020	1.050	1.072	1.102	1.138	1.192	1.378
Steifemodul [MN/m ²]		6.7	6.9	7.6	8.2	19.4	34.7	-	-	14.0	38.2	60.7	101.1	134.8	75.3

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 9,8
Probendurchmesser [mm] = 70	w (nachher) [%] = 9,0
