



# Druck-Setzungs-Versuch

## U 5 Ost E

Bearbeiter: Boe

Datum: 20.0.18


Auftragsnummer: 022445

Entnahmestelle: B 64/17


Tiefe [m]: 13,25

Labornummer: 16

Geolog. Bez.: Beckenschluff



Normalspannung [kN/m<sup>2</sup>] (logarithmisch)

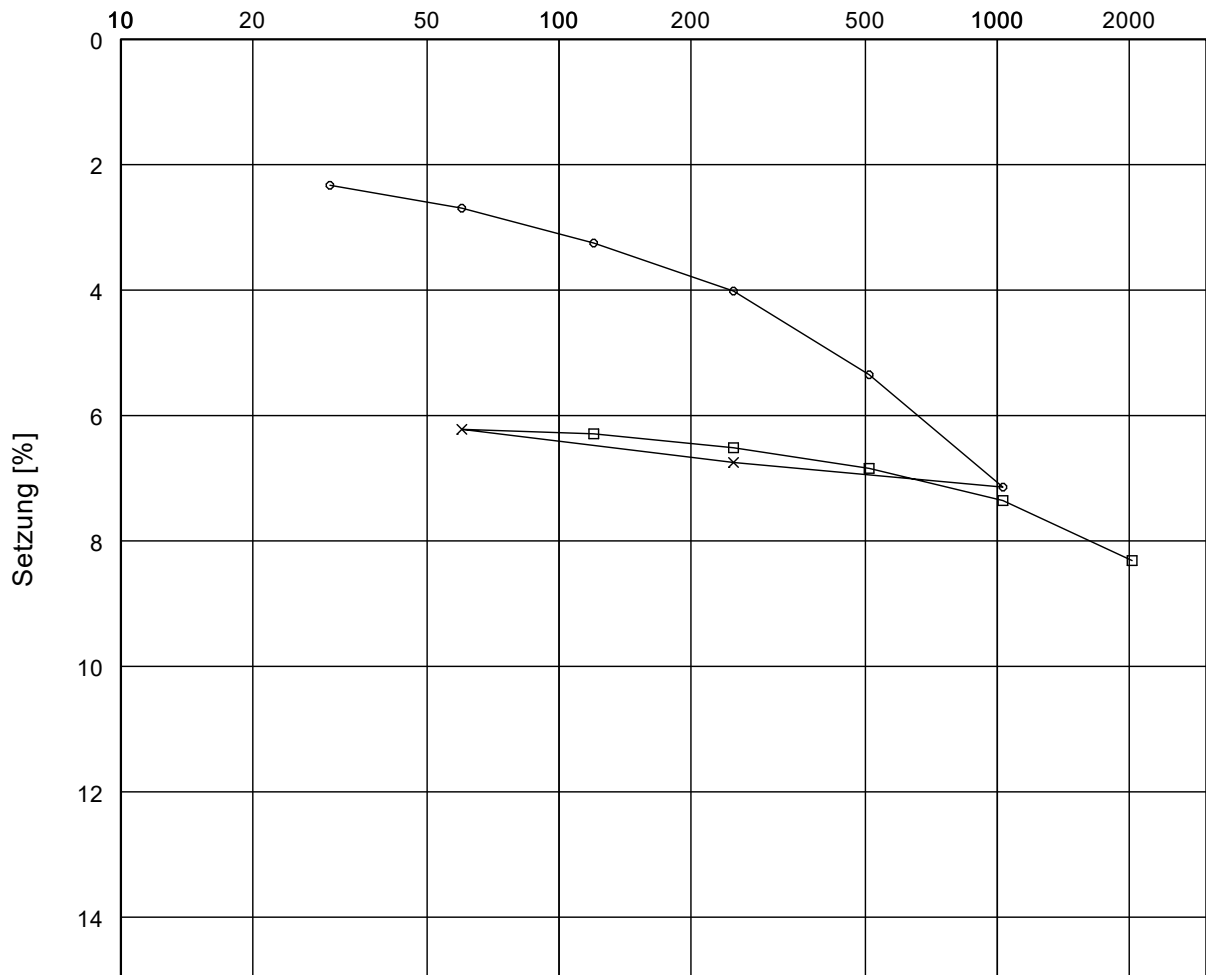

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13
Normalspannung [kN/m <sup>2</sup> ]	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.326	0.377	0.455	0.562	0.749	1.000	0.945	0.871	0.881	0.912	0.958	1.030	1.164
Steifemodul [MN/m <sup>2</sup> ]		8.2	10.8	17.0	19.5	29.0	-	-	84.0	58.7	79.1	101.1	104.5

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 17,6
Probendurchmesser [mm] = 70	w (nachher) [%] = 7,5
