



# Druck-Setzungs-Versuch

## U5 Ost E

Bearbeiter: Ti

Datum: 10.02.17


Auftragsnummer: 021785

Entnahmestelle: B 50

Tiefe: 35,25

Labornummer: 20

Geolog. Bez.: Lauenburger Ton

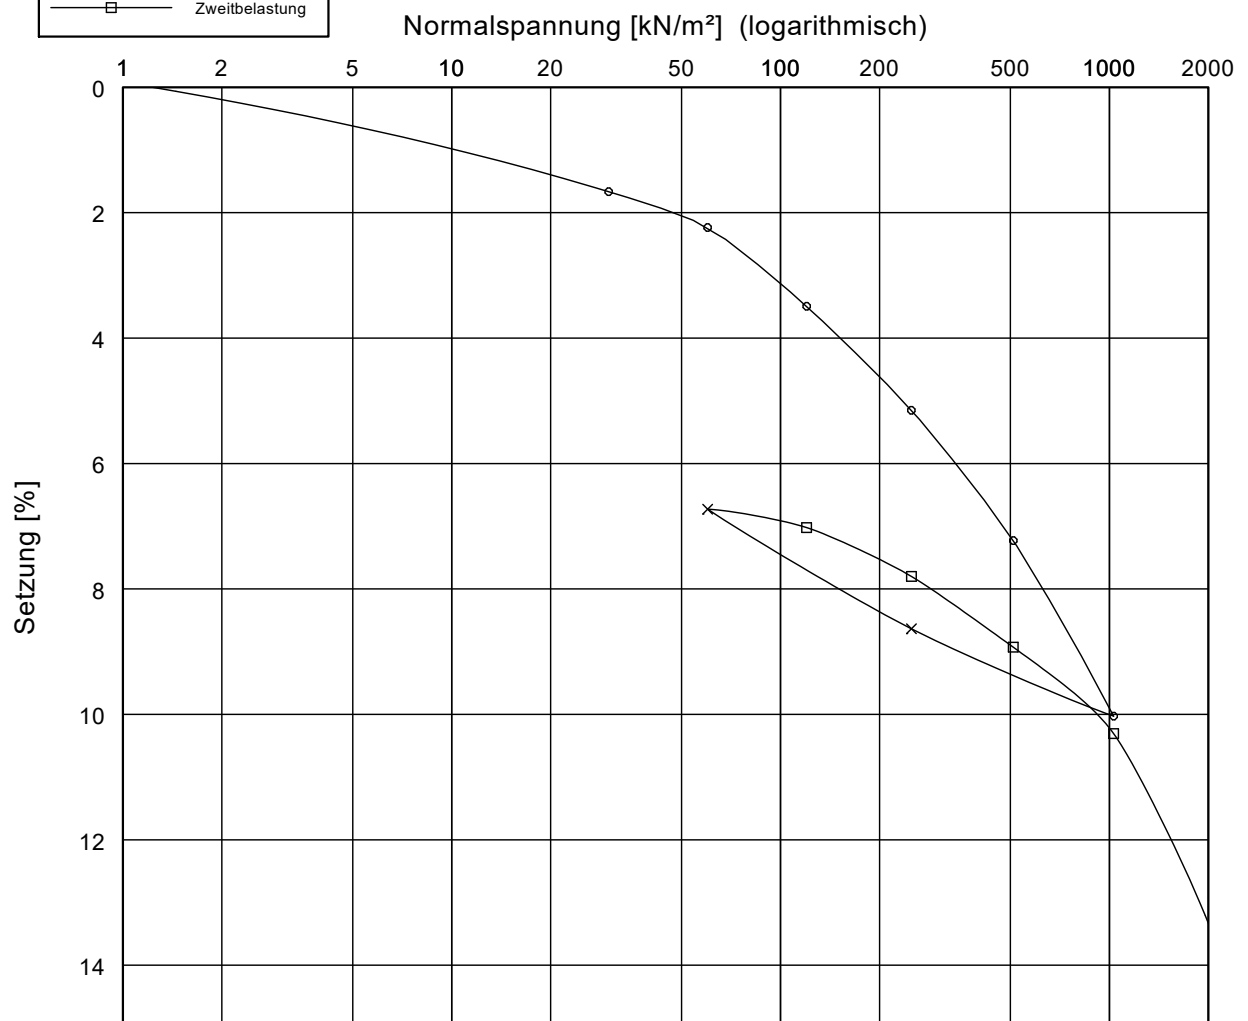

Versuch-Nr.	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Normalspannung [kN/m <sup>2</sup> ]	0.0	30.0	60.0	120.0	250.0	510.0	1030.0	250.0	60.0	120.0	250.0	510.0	1030.0	2030.0
Meßuhrablesung [mm]	0.000	0.233	0.313	0.489	0.721	1.012	1.404	1.209	0.942	0.983	1.092	1.250	1.443	1.879
Steifemodul [MN/m <sup>2</sup> ]		1.8	5.3	4.8	7.8	12.5	18.6	-	-	20.5	16.7	23.0	37.7	32.1

Einbauhöhe [mm] = 14.000	w (vorher) [%] = 27,8
Probendurchmesser [mm] = 70	w (nachher) [%] = 24,4
